


PROJECT: City of Norcross

Sunbelt Asphalt Schedule

Legend: On track Completed

Project start date: 10/27/2025

Scrolling increment: 0

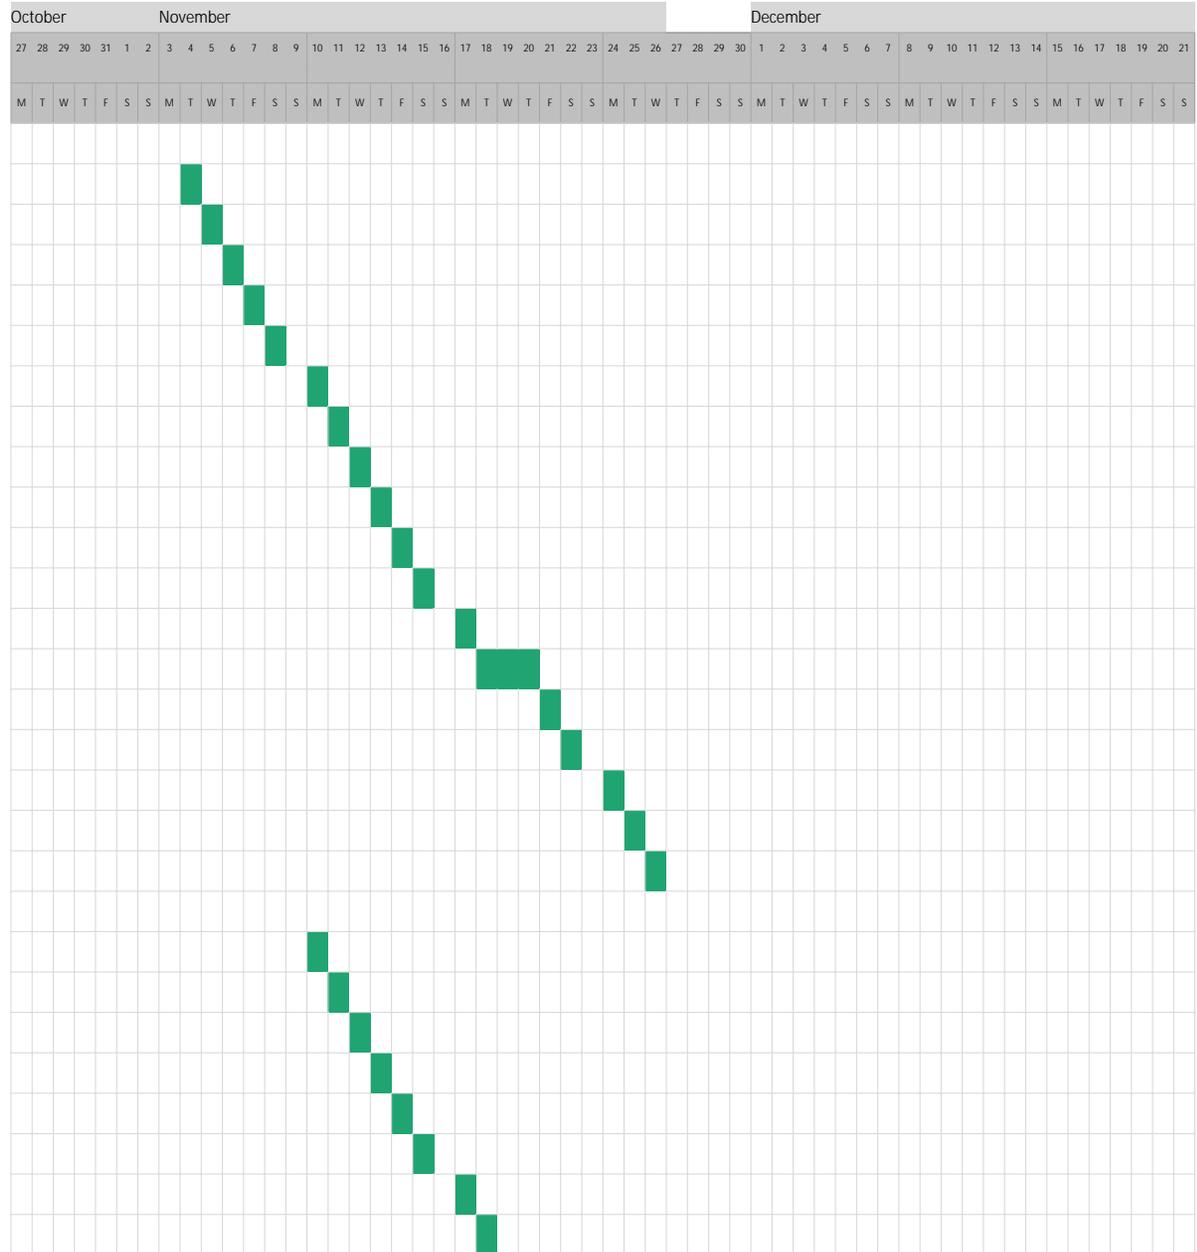

Milestone description	Category	Assigned to	Progress	Start	Days
Patching and Milling					
Kimberly Lane	On Track	Patching/Milling Crew	0%	11/4/2025	1
Sharon Drive	On Track	Patching/Milling Crew	0%	11/5/2025	1
Rockies Court	On Track	Patching/Milling Crew	0%	11/6/2025	1
Western Hills Ct	On Track	Patching/Milling Crew	0%	11/7/2025	1
Lancelot Drive	On Track	Patching/Milling Crew	0%	11/8/2025	1
Executive Way	On Track	Patching/Milling Crew	0%	11/10/2025	1
Landing Court	On Track	Patching/Milling Crew	0%	11/11/2025	1
Ballard Way	On Track	Patching/Milling Crew	0%	11/12/2025	1
Charmaine Bend	On Track	Patching/Milling Crew	0%	11/13/2025	1
Crest Trace Ct	On Track	Patching/Milling Crew	0%	11/14/2025	1
Hollow Ridge Drive	On Track	Patching/Milling Crew	0%	11/15/2025	1
Crest Hollow Court	On Track	Patching/Milling Crew	0%	11/17/2025	1
Goshen Springs Court	On Track	Patching/Milling Crew	0%	11/18/2025	3
Wexford Court	On Track	Patching/Milling Crew	0%	11/21/2025	1
Davidson Road	On Track	Patching/Milling Crew	0%	11/22/2025	1
Oak Cove	On Track	Patching/Milling Crew	0%	11/24/2025	1
Sunset Drive	On Track	Patching/Milling Crew	0%	11/25/2025	1
Queens Court	On Track	Patching/Milling Crew	0%	11/26/2025	1
Topping Crew					
Kimberly Lane	On Track	Topping	0%	11/10/2025	1
Sharon Drive	On Track	Topping	0%	11/11/2025	1
Rockies Court	On Track	Topping	0%	11/12/2025	1
Western Hills Ct	On Track	Topping	0%	11/13/2025	1
Lancelot Drive	On Track	Topping	0%	11/14/2025	1
Executive Way	On Track	Topping	0%	11/15/2025	1
Landing Court	On Track	Topping	0%	11/17/2025	1
Ballard Way	On Track	Topping	0%	11/18/2025	1

